

# EXHIBIT 10

TO

MEMORANDUM IN SUPPORT OF MOTION IN LIMINE TO ESTABLISH THE UNITED STATES' LEGAL ENTITLEMENT TO A FEDERAL RESERVED WATER RIGHT AND TO LIMIT THE SCOPE OF EVIDENCE NECESSARY AT TRIAL

Civil No. 05-cv-49053

CONSTRUCTION PROGRAM AT AIR CORPS STATIONS

No. 4 - Muroc Bombing Range, California

1. Location and general description of project:

Construction of temporary housing facilities, utilities and technical facilities for bombing range at Muroc Dry Lake, California.

2. Pertinent data:

Originally Authorized Work:

Date directive issued by A.G.O. to Q.M.C. - October 19, 1940

Construction begun:

Administrative and Housing - September 10, 1940  
Hospital or Medical Corps Installation - September 30, 1940  
Technical Facilities - October 14, 1940

Additional (new) Work:

Date directive issued by O. C. E. to D.E. - June 4, 1941

Construction begun:

Technical Facilities - Not yet started.

3. Status of construction:

Construction of Barracks, Dispensary, Railroad, Magazines, Fencing and appurtenant work. Entire project (originally authorized work) approximately 98% complete. Right-of-way available. Construction of Ordnance facilities, Target Installations, and Runways have been authorized but no work is under way.

4. Cost of project:

a. Authorized Cost: \$1,586,452.00  
b. Present estimated cost: \$2,220,162.00  
c. Estimated cost of work under way or completed under authorized project: \$ 445,933.00

5. Funds allotted to date: \$1,570,452.00

Subprocurement from Air Corps: \$ 16,000.00

Additional funds in the amount of \$1,177,000.00 for Runway construction received under Procurement Authority Eng.-1077 dated June 19, 1941.

CONSTRUCTION PROGRAM AT AIR CORPS STATIONS

No. 4 - Muroc Bombing Range, California (Cont'd)

6. Status of plans and specifications:

Specifications and plans were completed and invitations for bids were issued for Target installations, construction of Apron, Runways, and Taxiways, and construction of Ordnance Buildings, and appurtenant facilities.

7. Operations during this half-month period:

Construction of street improvements was continued. All other work originally authorized has been completed, and no work has been started on additional authorized construction. Bids were opened for Target installations, Runway construction, and Ordnance Buildings.

8. Probable operations next half-month:

Construction of Streets and Walks will be completed. Contractors for Runway construction, Ordnance Building construction, and Target installations will start work.

9. Estimated date of completion:

Originally Authorized Work:	
Administrative and Housing (including utilities)	- July 15, 1941
Hospital or Medical Corps facilities	- March 1, 1941
Technical facilities	- June 30, 1941
Originally authorized work	- July 15, 1941
Additional (new) work:	
Technical facilities	- Nov. 10, 1941
Project as a whole	- Nov. 10, 1941

10. Remarks:

Purchase order issued for installation of beacon light and electrical hook-up on the elevated water tank. Authority has been requested and received for construction by supplemental agreement of an A. C. Gasoline System consisting of four 25,000 gallon tanks, four double pit fills, and one double truck fill, at an estimated cost of \$77,000.00.

CONSTRUCTION PROGRAM AT AIR CORPS STATIONS

No. 4 - Muroc Bombing Range, California (Cont'd)

10. Remarks: (Cont'd)

Employment data:

a.	Architect-Engineers' Employees	None
b.	Construction Contractor's	5
c.	W.P.A. Employees	None
d.	Hired Labor	None
e.	Project & District Overhead (Including Engineering)	7

WAR DEPARTMENT

CORPS OF ENGINEERS, U.S. ARMY


Muroo Bombing Range


PROGRESS CHART FOR PERIOD June 16-30, 1941

LEGEND:-  
 WORK COMPLETED PREVIOUSLY [Solid Black Box] COMPLETED THIS HALF MONTH [Diagonal Lines Box]  
 PROBABLE NEXT HALF MONTH [Dotted Box]

ITEMS	NUMBER OR QUANTITY	PERCENT COMPLETED			
		25	50	75	100
ADMINISTRATIVE & HOUSING					
ORIGINAL AUTHORITY					
Barracks, 63 man	4				
Mess Halls, 170 man	1				
Recreation Bldg, 250 man	1				
Radio Transmitter Bldg	1				
Water System	1				
Well	1				
High Tank & Trestle	1				
Sewer, Gas, Irrigation	1				
Sewage Disposal Plant	1				
Electrical Distribution	1				
Propane Plant	1				
Fence, Ord. Mag. Area	1				
Fence, Radio Range Area	1				
Railroad Spur	1				
Roads & Streets	1				
PROGRESS - Original Authority					
NEW PROJECTS (None)					
HOSPITAL FACILITIES					
ORIGINAL AUTHORITY					
Dispensary	1				
PROGRESS - Original Authority					
NEW PROJECTS (None)					
TECHNICAL FACILITIES					
ORIGINAL AUTHORITY					
Ordnance Magazines	6				
PROGRESS - Original Authority					
NEW PROJECTS					
Aerial Targets	4				
Runway, Aprons	1				
Add. Ordnance Facilities	1				
Observation Tower	1				
PROGRESS - New Projects					
COMPLETE AIRFIELD					
ORIGINAL AUTHORITY					
NEW PROJECTS					

#13

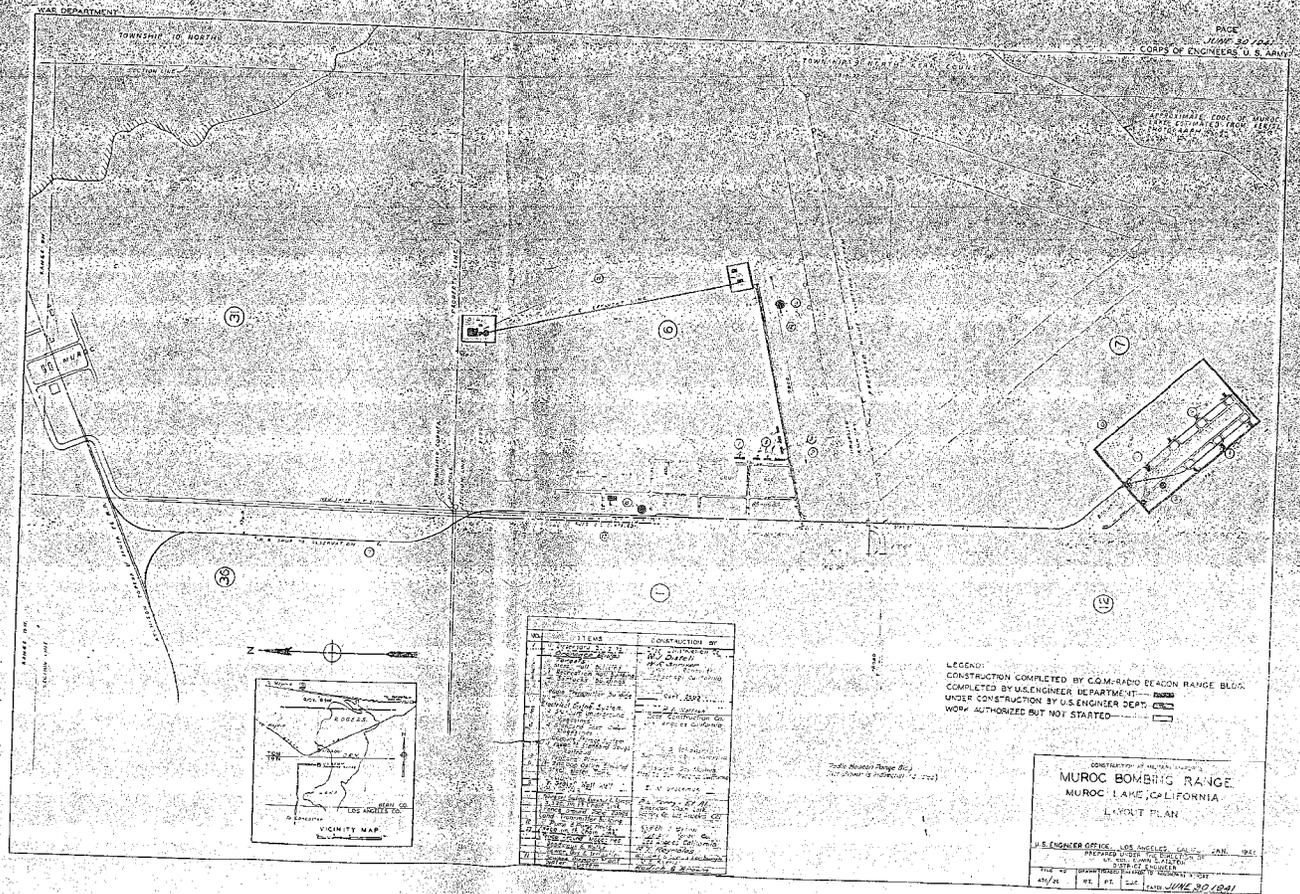

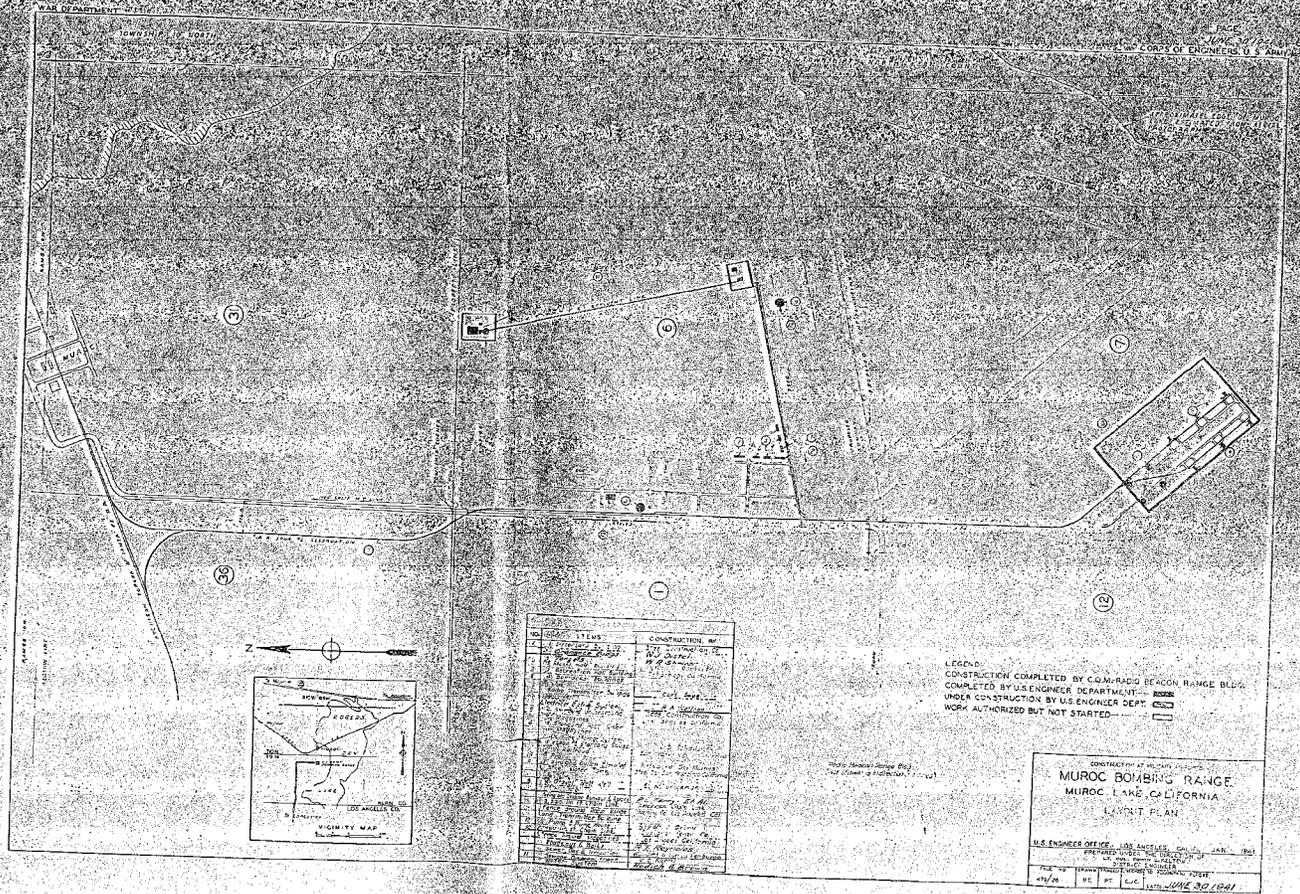

ITEM NO.	DESCRIPTION	CONSTRUCTION BY
1	Runway 1	U.S. Army
2	Runway 2	U.S. Army
3	Runway 3	U.S. Army
4	Runway 4	U.S. Army
5	Runway 5	U.S. Army
6	Runway 6	U.S. Army
7	Runway 7	U.S. Army
8	Runway 8	U.S. Army
9	Runway 9	U.S. Army
10	Runway 10	U.S. Army

LEGEND:  
 CONSTRUCTION COMPLETED BY COM-RANGS BEACON RANGE BLDG.  
 COMPLETED BY U.S. ENGINEER DEPARTMENT - BDRB  
 UNDER CONSTRUCTION BY U.S. ENGINEER DEPT. - BDRB  
 WORK AUTHORIZED BUT NOT STARTED - BDRB

CONSTRUCTION AT MUROC BOMBING RANGE  
**MUROC BOMBING RANGE**  
 MUROC LAKE, CALIFORNIA  
 LAYOUT PLAN  
 U.S. ENGINEER OFFICE, LOS ANGELES, CALIF., JAN. 1951  
 PREPARED UNDER THE DIRECTION  
 OF THE CHIEF OF ENGINEERS  
 U.S. ARMY CORPS OF ENGINEERS  
 FILE NO. 474/28 ST. PT. CUC. DATE: 1/19/51

10/1/40

EAFO History Center Kelly 1405  
(Box) EDW: [Munz AAF] WWII 1940-  
(Box) 70 The Edwards Munz AAF  
(General Correspondence)
